Cost Variance Report

Customer Portal Rebuild

Q1-Q2 2026 rebuild of the customer self-service portal.

Generated 2026-10-26 07:46 UTC

Estimated	Actual	Variance	Variance %
100,000.00	112,200.00	+12,200.00	+12.2%

18 items: 7 over budget, 8 on budget (within 5%), 3 under budget.

AI cost analysis

Overview: Customer Portal Rebuild is over budget. Estimated 100,000 vs actual 112,200, a variance of 12,200 (+12.2%) across 18 items.

Key drivers:
- Labour overran by 3,900 (+5.95%).
- Contingency overran by 3,800 (no estimate).
- Software overran by 2,400 (+23.08%).
- Hardware came in 270 under (-3%).

Unusual expenses:
- Emergency data recovery (Contingency): Unbudgeted expense (estimate was 0); Overrun of 3800.00 is far above typical items (fence 2072.5).
- Backend development (Labour): Overrun of 3600.00 is far above typical items (fence 2072.5).
- Monitoring SaaS (Software): Variance 227.78% is an unusual overrun (z = 3.81).

Recommendations:
- Review scope and estimating assumptions for Labour.
- Verify the flagged items against invoices before sign-off.

AI service not configured; rule-based summary shown.

By category

Category	Items	Estimated	Actual	Variance	Variance %
Labour	5	65,500.00	69,400.00	3,900.00	+6.0%
Software	4	10,400.00	12,800.00	2,400.00	+23.1%
Consulting	2	8,500.00	8,750.00	250.00	+2.9%
Hardware	2	9,000.00	8,730.00	-270.00	-3.0%
Travel	1	3,000.00	4,900.00	1,900.00	+63.3%
Contingency	1	0.00	3,800.00	3,800.00	n/a
Training	2	3,200.00	3,400.00	200.00	+6.3%
Other	1	400.00	420.00	20.00	+5.0%


Unusual expenses (3)

Emergency data recovery (Contingency) est 0.00 / act 3,800.00 / n/a
Unbudgeted expense (estimate was 0); Overrun of 3800.00 is far above typical items (fence 2072.5)


Backend development (Labour) est 24,000.00 / act 27,600.00 / +15.0%
Overrun of 3600.00 is far above typical items (fence 2072.5)

Monitoring SaaS (Software) est 900.00 / act 2,950.00 / +227.8%
Variance 227.78% is an unusual overrun (z = 3.81)


Estimated vs actual by category

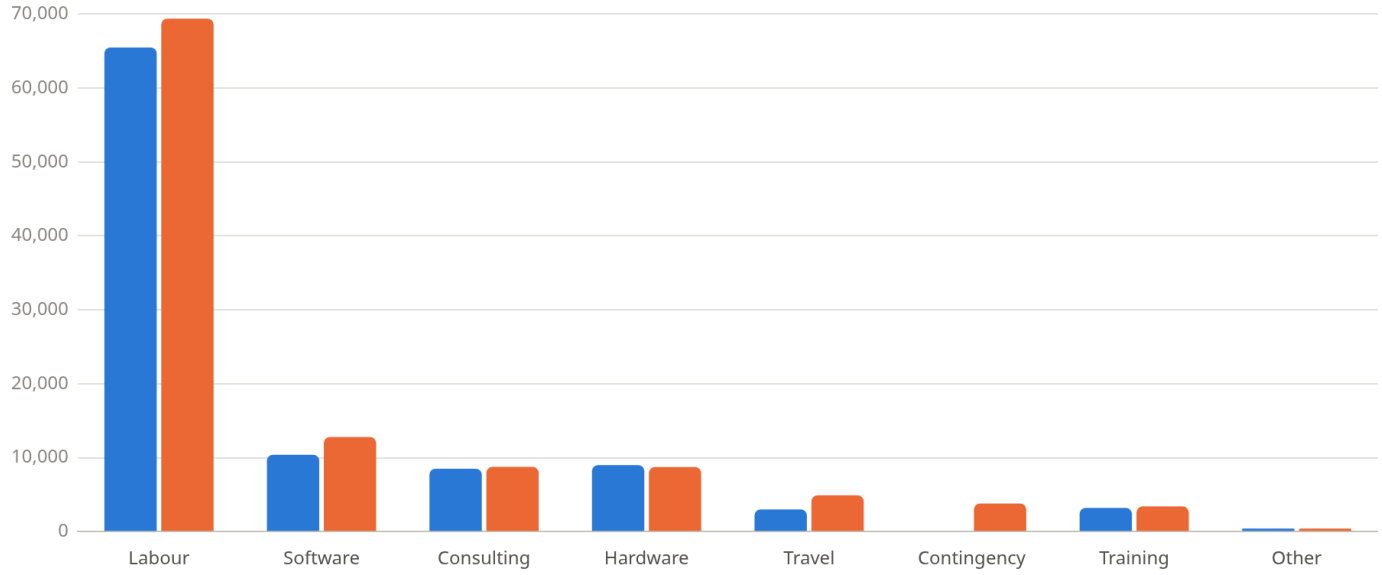

Variance by category

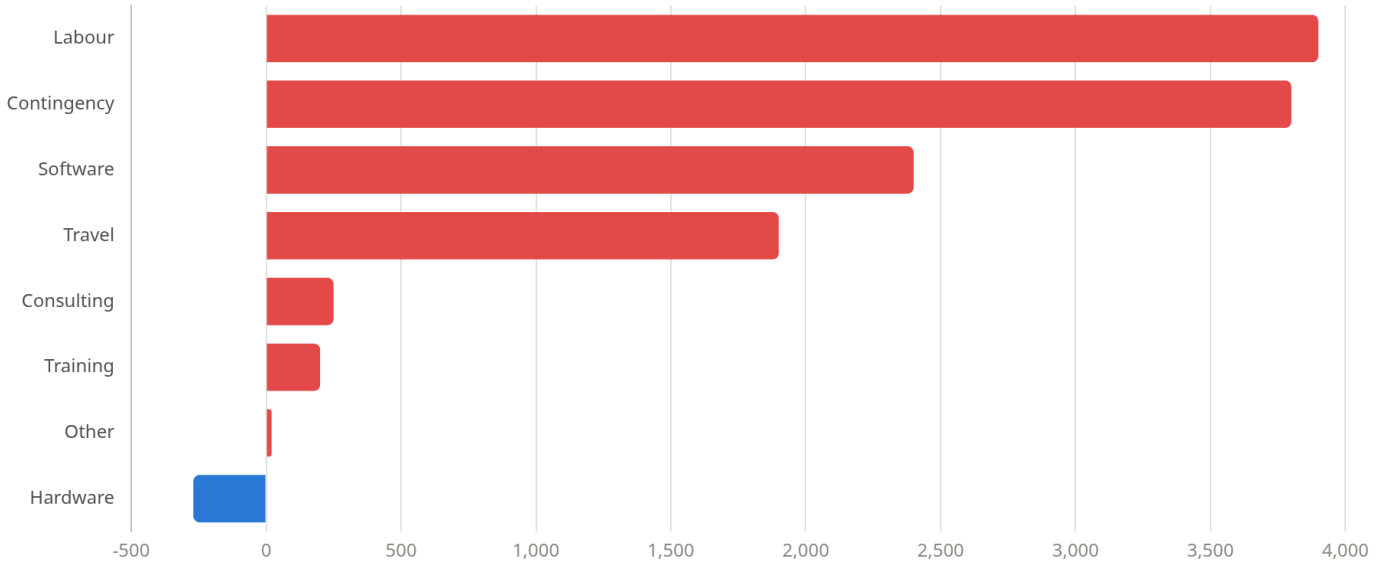

Variance % per line item

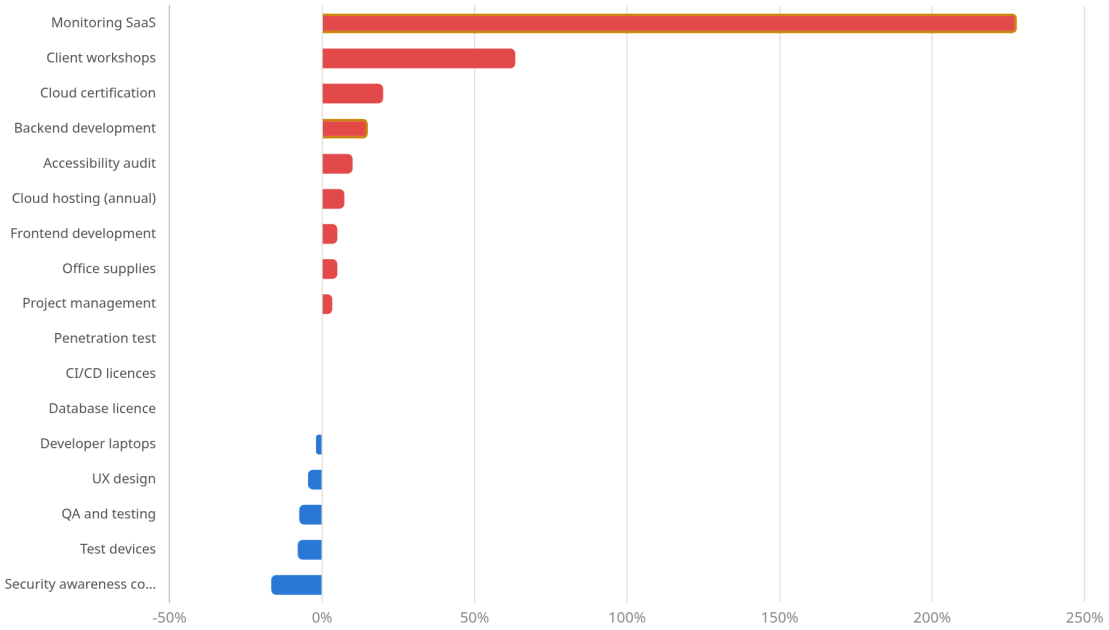

Line items

Category	Item	Estimated	Actual	Variance	Var %	Status
Consulting	Penetration test	6,000.00	6,000.00	0.00	0.0%	On budget
Consulting	Accessibility audit	2,500.00	2,750.00	250.00	+10.0%	Over
Contingency	Emergency data recovery	0.00	3,800.00	3,800.00	n/a	Over
Hardware	Developer laptops	7,500.00	7,350.00	-150.00	-2.0%	On budget
Hardware	Test devices	1,500.00	1,380.00	-120.00	-8.0%	Under
Labour	Backend development	24,000.00	27,600.00	3,600.00	+15.0%	Over
Labour	Frontend development	18,000.00	18,900.00	900.00	+5.0%	On budget
Labour	QA and testing	8,000.00	7,400.00	-600.00	-7.5%	Under
Labour	Project management	9,000.00	9,300.00	300.00	+3.3%	On budget
Labour	UX design	6,500.00	6,200.00	-300.00	-4.6%	On budget
Other	Office supplies	400.00	420.00	20.00	+5.0%	On budget
Software	Cloud hosting (annual)	4,800.00	5,150.00	350.00	+7.3%	Over
Software	CI/CD licences	1,200.00	1,200.00	0.00	0.0%	On budget
Software	Monitoring SaaS	900.00	2,950.00	2,050.00	+227.8%	Over
Software	Database licence	3,500.00	3,500.00	0.00	0.0%	On budget
Training	Security awareness course	1,200.00	1,000.00	-200.00	-16.7%	Under
Training	Cloud certification	2,000.00	2,400.00	400.00	+20.0%	Over
Travel	Client workshops	3,000.00	4,900.00	1,900.00	+63.3%	Over
